
Blood Bank and Donor Management System

Project Schedule and Work Breakdown Structure(WBS)

The Blood Bank and Donor Management System (BBDMS) is a web-based platform for managing donor records, blood inventory, donation scheduling and emergency blood requests. This document presents the project schedule and the work breakdown structure used to plan and track its delivery.

1. Project Schedule

The Gantt chart lists each activity with its duration, predecessors and dates. The project runs for 77 days, from 17 Aug 2026 to 31 Oct 2026, moving from planning through development, testing, deployment and maintenance.

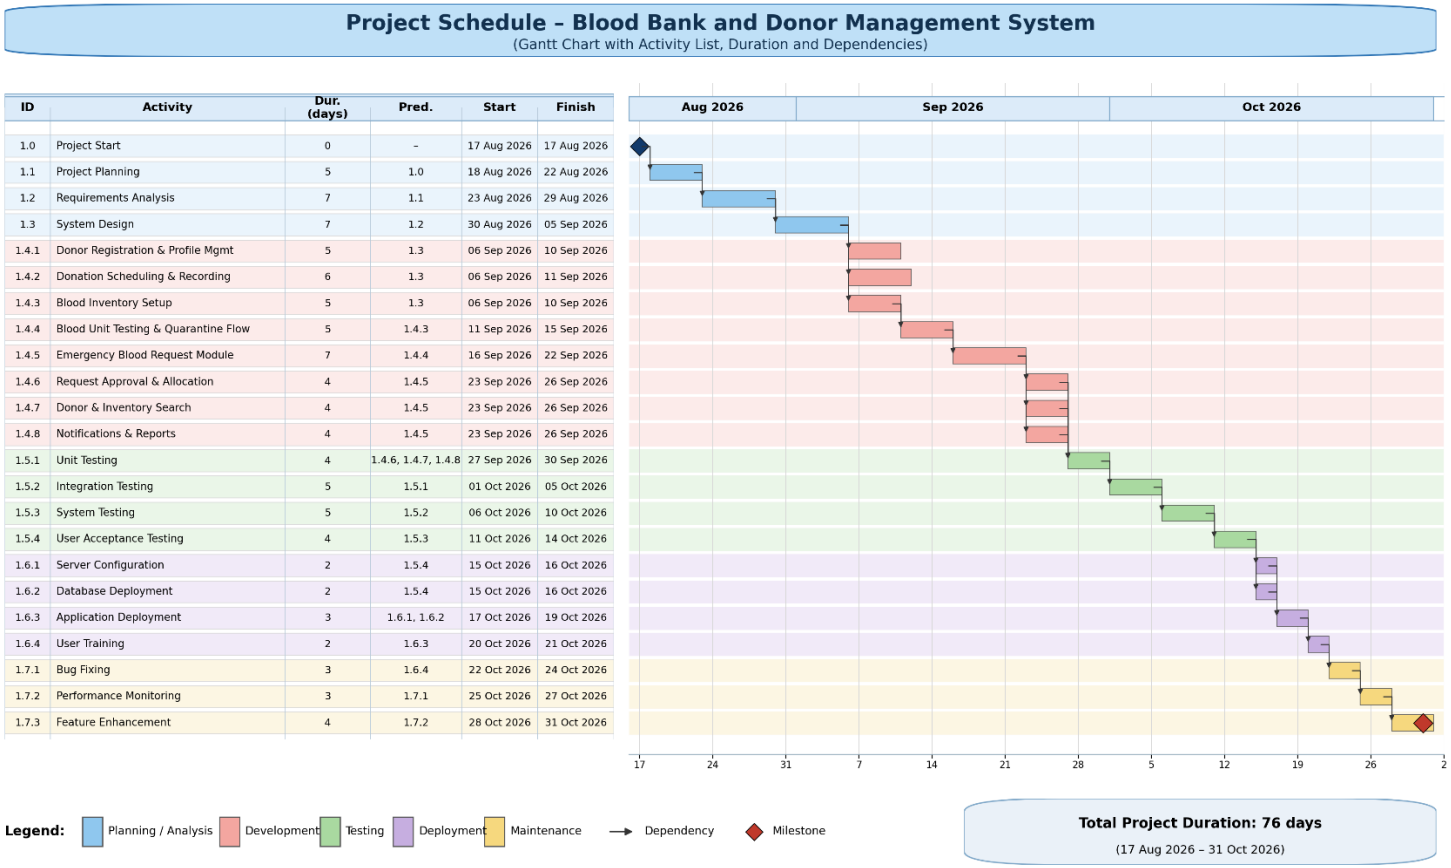

ID	Activity	Dur. (days)	Pred.	Start	Finish
1.0	Project Start	0	-	17 Aug 2026	17 Aug 2026
1.1	Project Planning	5	1.0	18 Aug 2026	22 Aug 2026
1.2	Requirements Analysis	7	1.1	23 Aug 2026	29 Aug 2026
1.3	System Design	7	1.2	30 Aug 2026	05 Sep 2026
1.4.1	Donor Registration & Profile Mgmt	5	1.3	06 Sep 2026	10 Sep 2026
1.4.2	Donation Scheduling & Recording	6	1.3	06 Sep 2026	11 Sep 2026
1.4.3	Blood Inventory Setup	5	1.3	06 Sep 2026	10 Sep 2026
1.4.4	Blood Unit Testing & Quarantine Flow	5	1.4.3	11 Sep 2026	15 Sep 2026
1.4.5	Emergency Blood Request Module	7	1.4.4	16 Sep 2026	22 Sep 2026
1.4.6	Request Approval & Allocation	4	1.4.5	23 Sep 2026	26 Sep 2026
1.4.7	Donor & Inventory Search	4	1.4.5	23 Sep 2026	26 Sep 2026
1.4.8	Notifications & Reports	4	1.4.5	23 Sep 2026	26 Sep 2026
1.5.1	Unit Testing	4	1.4.6, 1.4.7, 1.4.8	27 Sep 2026	30 Sep 2026
1.5.2	Integration Testing	5	1.5.1	01 Oct 2026	05 Oct 2026
1.5.3	System Testing	5	1.5.2	06 Oct 2026	10 Oct 2026
1.5.4	User Acceptance Testing	4	1.5.3	11 Oct 2026	14 Oct 2026
1.6.1	Server Configuration	2	1.5.4	15 Oct 2026	16 Oct 2026
1.6.2	Database Deployment	2	1.5.4	15 Oct 2026	16 Oct 2026
1.6.3	Application Deployment	3	1.6.1, 1.6.2	17 Oct 2026	19 Oct 2026
1.6.4	User Training	2	1.6.3	20 Oct 2026	21 Oct 2026
1.7.1	Bug Fixing	3	1.6.4	22 Oct 2026	24 Oct 2026
1.7.2	Performance Monitoring	3	1.7.1	25 Oct 2026	27 Oct 2026
1.7.3	Feature Enhancement	4	1.7.2	28 Oct 2026	31 Oct 2026

Figure 1: Project schedule (Gantt chart)

2. Work Breakdown Structure

The WBS splits the project into seven major phases, each broken down into work packages: planning, requirements analysis, system design, development, testing, deployment and maintenance.

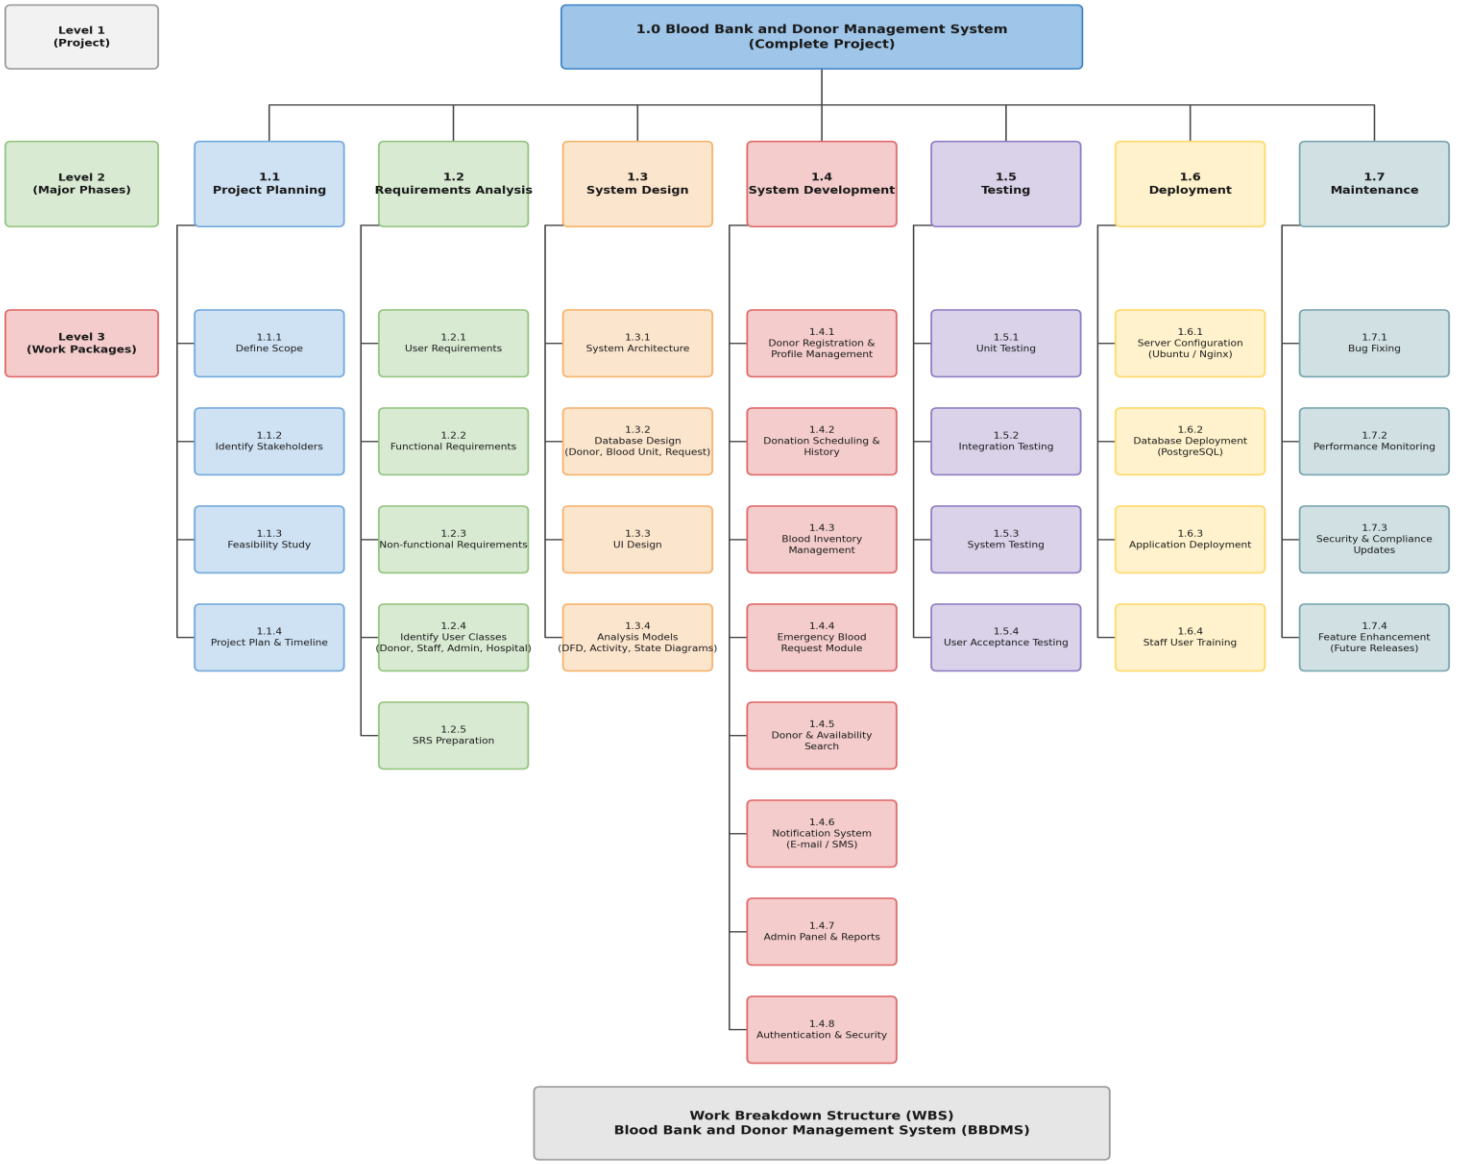


Figure 2: Work Breakdown Structure (WBS)
